



Perry County Courthouse Weekly Summary

Updated 1/10/25

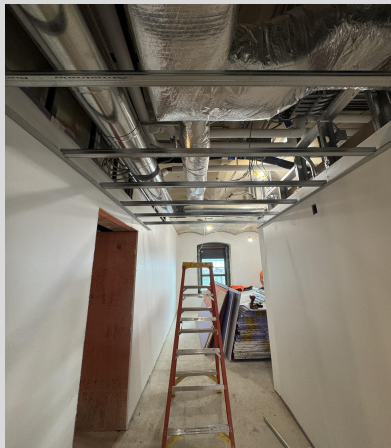

Ground
Floor
Ceiling
Install
1/10/25

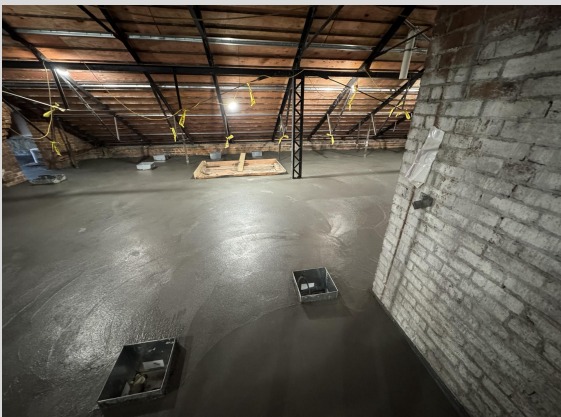

South Attic Concrete Pour 1/2/25



Permanent Power Excavation 1/10/25

Construction Activities

- Electricians Continued Rough-In On 1st Floor And Trench Excavation For Permanent Power.
- HVAC Crew Continued Running Duct On 1st Floor And Refrigerant Lines In The Attic.
- CK Framers Continued Ceiling & Wall Framing Ground Floor.
- CK Steel Crew Continued SOMD Install On The 2nd Floor.
- Exterior Masons Finished Tuckpointing On The East & South Elevations.
- Roofers Finished Copper Flashing & Continued Install Of Copper Gutters.
- Interior Masons Continued Arch Stabilization On The 1st Floor & 2nd Floor.
- Painters Continued Prime & 1st Coat On The Ground & 1st Floor.

Total Manhours Worked To Date

- 49,812.38 Hours

Request For Information (RFI's)

- 9 Open RFI's

Submittals

- 0 Open Submittals

Weekly Weather Report

- Working Days Lost This Week: 1

Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
