


# Perry County Courthouse Weekly Summary

Updated 4/4/25



Elevator Install 4/4/25

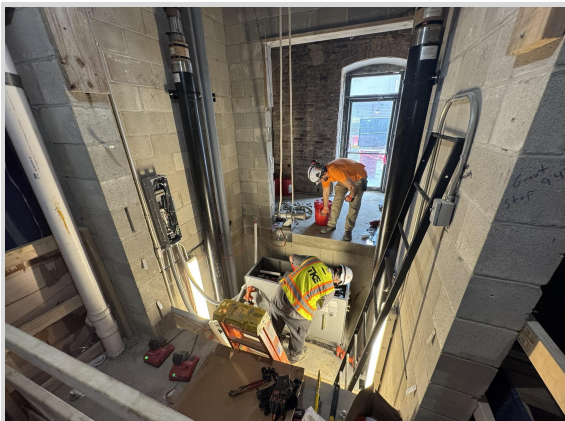

Ground Floor  
Doorway  
Lintel 4/4/25



2<sup>nd</sup> Floor Courtroom Window Removal  
4/4/25

## Construction Activities

- Electricians Continued 1<sup>st</sup> Floor 2<sup>nd</sup> Floor Rough-In. Low Voltage Electricians Continued Pulling Wire On The 1<sup>st</sup> Floor.
- HVAC Crew Continued Ductwork On The 1<sup>st</sup> Floor And Refrigeration Lines In The Attic.
- CK Framers Continued Ceilings On The Ground & 2<sup>nd</sup> Floor, And Framing Walls Around The Elevator Shaft.
- CK Carpenters Continued Window Trim Installation And Door Refinishing.
- Painters Continued Priming & 1<sup>st</sup> Coat Of Existing Ground Floor Ceilings.
- Scaffolding Erectors Finished Teardown Of The Exterior Scaffold.
- Elevator Technicians Began Elevator Install.
- Interior Masons Installed A Doorway Lintel On The Ground Floor.

## Total Manhours Worked To Date

- 62,770 Hours

## Request For Information (RFI's)

- 6 Open RFI's

## Submittals

- 2 Open Submittals

## Weekly Weather Report

- Working Days Lost This Week: None

## Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
