


Perry County Courthouse Weekly Summary

Updated 8/30/24



Elevator & Egress Stair Floor Demo
8/30/24

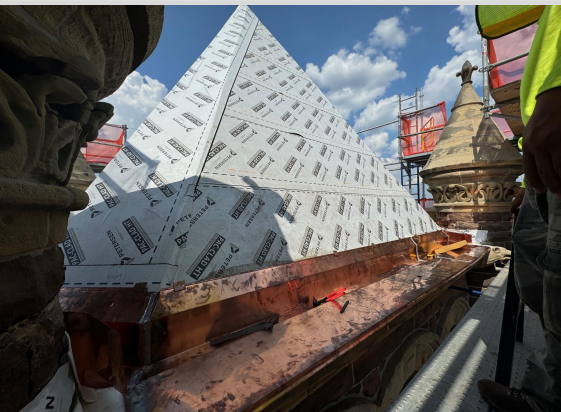

Clock Tower Copper Gutter 8/30/24



Ground Floor Corridor Plaster Repair
8/30/24

Construction Activities

- Electricians Continued Roughing In Walls On The Ground, 1st, And 2nd Floor.
- CK Carpenters Continued Wood Restoration On The Second Floor.
- CK Steel Crew Began Install Of Lateral Bracing On The 2nd Floor.
- Plaster Crew Continued Patching On The Ground Floor And 2nd Floor Courtroom.
- Painters Continued Priming New Wood Base.
- Exterior Masons Began Disassembly Of Clock Tower Clock Face's.
- Roofers Finished Installed Roof Sheathing And Began Copper Gutter.
- Demo Crew Began Floor Demo For Elevator & Egress Stair.

Total Manhours Worked To Date

- 30,132 Hours

Request For Information (RFI's)

- 3 Open RFI's

Submittals

- 1 Open Submittal

Weekly Weather Report

- Working Days Lost This Week: 0

Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
