

Perry County Courthouse Weekly Summary


Updated 10/25/24



West Elevation Gutter Install 10/25/24



Magistrate Court Steel 10/25/24

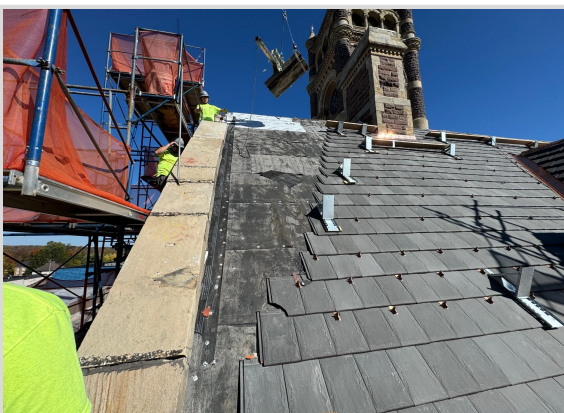

North Gable Stone Reset 10/22/24

Construction Activities

- Electricians Continued Roughing-In Walls On The Ground, 1st, And 2nd Floor.
- Electricians Continued Installation Of Lighting Protection System.
- HVAC Crew Continued Piping And Duct Work Install On The Ground And 1st And 2nd Floor.
- CK Steel Crew Finished Steel Install In The Magistrate Courtroom On The 1st Floor And Continued Steel Decking In The Attic.
- Plaster Crew Continued Plaster Restoration On The Ground, 1st, And 2nd Floor.
- Exterior Masons Finished Clock Tower Restoration Work, Reset The North Gable Cap Stones, And Continued Restoration On The West And North Elevation Of The Building.
- Interior Masons Continued HVAC Lintel Install, And Grouted The Magistrate Court Pinch Beam.
- Plumbers Continued 1st And 2nd Floor Plumbing Rough-In.

Total Manhours Worked To Date

- 39,400 Hours

Request For Information (RFI's)

- 13 Open RFI's

Submittals

- 6 Open Submittals

Weekly Weather Report

- Working Days Lost This Week: 0

Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
