


Perry County Courthouse Weekly Summary

Updated 2/14/25



Shaft Wall Install 2/14/25

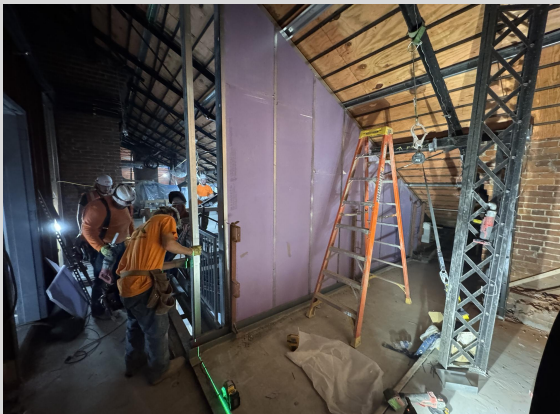

Spray Foam Installation 2/14/25



Water Meter Room Concrete Pour 2/14/25

Construction Activities

- Electricians Continued Rough-In On 2nd Floor And Conduit Layout For Exterior Underground Power.
- HVAC Crew Continued Running Duct On 1st Floor And Refrigerant Lines In The Attic.
- CK Framers Continued Shaft Wall Framing At The Egress Stair And Continued Walls On The Ground Floor.
- CK Steel Crew Continued Egress Stair Installation And Arch Stabilization.
- CK Concrete Crew Poured Water Meter Room On The Ground Floor.
- Interior Plumbers Continued 1st Floor Plumbing Rough In.
- Interior Masons Continued Arch Stabilization And Arch Removal On The 1st Floor.
- Window Installers Continued Placing Windows On The 1st Floor.
- Insulation Installers Began Spray Foaming The Attic Space.
- Roofers Continued Copper Downspout Install On The West Elevation.

Total Manhours Worked To Date

- 54,857 Hours

Request For Information (RFI's)

- 9 Open RFI's

Submittals

- 15 Open Submittals

Weekly Weather Report

- Working Days Lost This Week:

Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
