


# Perry County Courthouse Weekly Summary

Updated 2/21/25



Shaft Wall Install 2/21/25

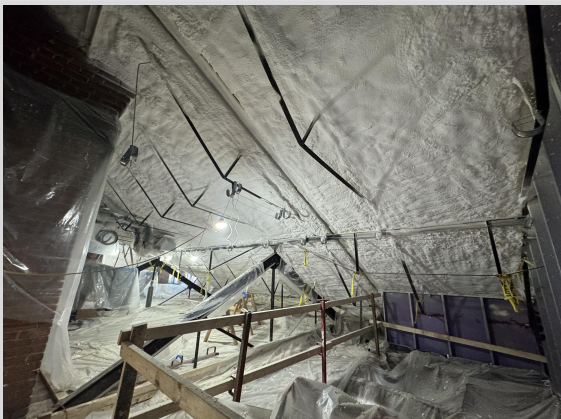

Spray Foam Installation 2/21/25



Existing  
Door Frame  
Painting  
2/21/25

## Construction Activities

- Electricians Continued Rough-In On 2nd Floor And Conduit Layout For Exterior Underground Power.
- HVAC Crew Built Ductwork Offsite.
- CK Framers Continued Shaft Wall Framing At The Egress Stair And Began Ceilings On The 2<sup>nd</sup> Floor.
- CK Steel Crew Finished Egress Stair Installation And Arch Stabilization.
- Interior Plumbers Continued 1<sup>st</sup> Floor Plumbing Rough In.
- Interior Masons Continued Arch Stabilization And Finished Walkway Removal On The 1<sup>st</sup> Floor.
- Window Installers Continued Placing Windows On The Ground & 1<sup>st</sup> Floor.
- Painters Continued Priming & 1<sup>st</sup> Coat Of Existing Door Frames On The 1<sup>st</sup> Floor.
- Insulation Installers Finished Spray Foaming The Attic Space.
- Roofers Finished Tile & Flashing Installation And Continued Copper Downspout Install On The West Elevation.

## Total Manhours Worked To Date

- 55,427 Hours

## Request For Information (RFI's)

- 10 Open RFI's

## Submittals

- 17 Open Submittals

## Weekly Weather Report

- Working Days Lost This Week: None

## Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
