


Perry County Courthouse Weekly Summary

Updated 3/21/25



East Elevation Window Trim Install
3/21/25

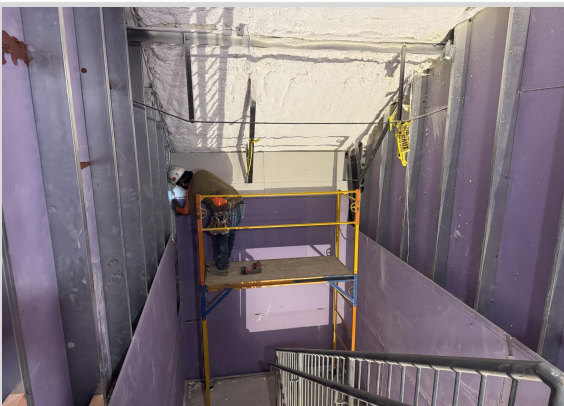

Egress Stair Installment 3/21/25



2nd Floor Courtroom Ceiling Painting
3/21/25

Construction Activities

- Electricians Finished Rough-in Of Elevator Lights/Power And Continued 1st Floor Power Rough-in.
- HVAC Crew Continued Ductwork On The 1st & 2nd Floor And Refrigeration Lines In The Attic.
- CK Framers Continued Shaft Wall Framing At The Egress Stair And Continued Ceilings On The 2nd Floor.
- CK Carpenters Continued Window Trim Installation And Door Refinishing.
- Window Installers Finished Window Installment & Caulking On The North Elevation.
- Painters Continued Priming & 1st Coat Of Existing 2nd Floor Courtroom Ceiling.
- Scaffolding Erectors Finished Teardown Of South Elevation Scaffolding, And Began East Elevation Teardown.

Total Manhours Worked To Date

- 60,495 Hours

Request For Information (RFI's)

- 4 Open RFI's

Submittals

- 5 Open Submittals

Weekly Weather Report

- Working Days Lost This Week: None

Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
