

# Perry County Courthouse Weekly Summary


Updated 3/7/25



North  
Elevation  
Storm  
Line Install  
3/7/25



Egress Stair  
Concrete  
Pour  
3/7/25

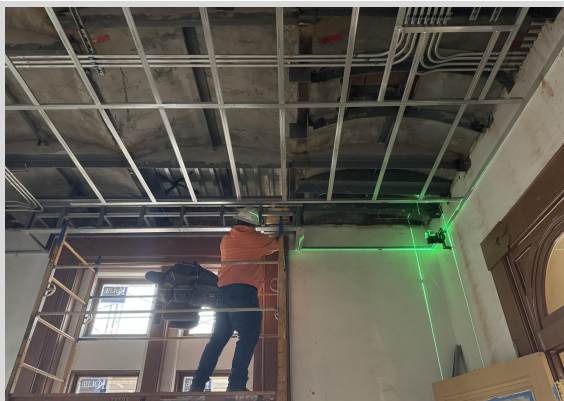

2<sup>nd</sup> Floor Ceiling Framing 3/7/25

## Construction Activities

- Electricians Continued Rough-In On 2<sup>nd</sup> Floor And Began Panel Wiring For Permanent Power.
- HVAC Crew Continued Ductwork On The 2<sup>nd</sup> Floor And Refrigeration Lines In The Attic.
- CK Concrete Crew Poured Steel Pans For The Egress Stair.
- CK Framers Continued Shaft Wall Framing At The Egress Stair And Continued Ceilings On The 2<sup>nd</sup> Floor.
- CK Carpenters Continued Window Trim Installation And Door Refinishing.
- Interior Plumbers Finished Water Meter Install.
- Exterior Plumbers Began Install Of The Storm Sewer On North Elevation
- Window Installers Began Installing Windows On The Ground & 1<sup>st</sup> Floor On The North Elevation.
- Painters Continued Priming & 1<sup>st</sup> Coat Of Existing Door Frames And Walls On The Ground & 1<sup>st</sup> Floor.

## Total Manhours Worked To Date

- 57,747 Hours

## Request For Information (RFI's)

- 8 Open RFI's

## Submittals

- 3 Open Submittals

## Weekly Weather Report

- Working Days Lost This Week: None

## Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
