


Perry County Courthouse Weekly Summary

Updated 4/11/25



Historic Newel Post Layout 4/11/25

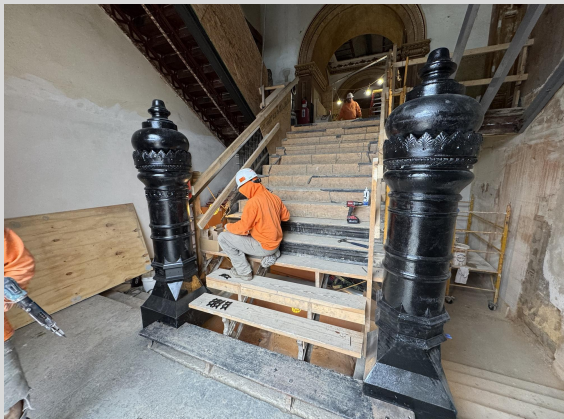

Historic Stair
Stringer
Install
4/11/25



Corridor
Stabilization
Installation
4/11/25

Construction Activities

- Electricians Finished First Floor Above Ceiling Rough-In And Continued 2nd Floor Rough-In. Low Voltage Electricians Finished Pulling Wire On The 1st Floor.
- HVAC Crew Continued Ductwork On The 1st Floor And Refrigeration Lines In The Attic.
- CK Framers Began Install Of The Drywall On The 1st Floor Ceilings, And Continued Framing On The 2nd Floor.
- CK Carpenters Continued Window Trim Installation, Door Casing Install, And Began Layout Of Historic Newel Posts.
- Painters Continued Priming & 1st Coat Of Existing Ground Floor Ceilings.
- Elevator Technicians Continued Elevator Install.
- Interior Masons Parged The Arches In The Bell Tower.

Total Manhours Worked To Date

- 64,902 Hours

Request For Information (RFI's)

- 11 Open RFI's

Submittals

- 4 Open Submittals

Weekly Weather Report

- Working Days Lost This Week: None

Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
