

Perry County Courthouse Weekly Summary


Updated 6/14/24



Roofing Tile Installation 6/13/24



Concrete Slab Preparation 6/14/24

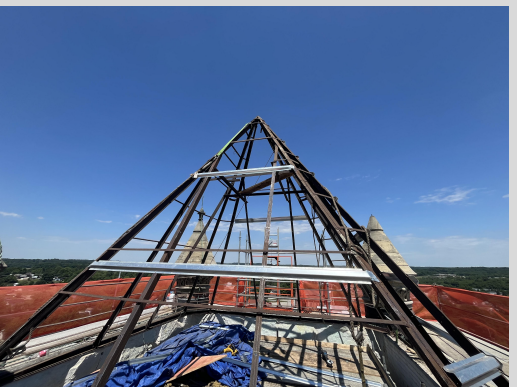

Exposed Bell Tower Roof 6/13/24

Construction Activities

- Scaffolding Erectors Installed Interior Clock Tower Scaffolding And Tore Down Scaffolding Around Tower Chimneys.
- Roofers Started Clock Tower Roof Restoration Per RFI Response.
- Roofers Started Tile Installation On Towers And Continued Box Gutter Installation On North and East Side Of Courthouse.
- Interior Masons Started Lintel Installation On Ground Floor Openings.
- Exterior Masons Finished Chimney Restoration And Continued Work On The Gables.
- Concrete Crew Continued Prep Work On Ground Floor For New Concrete Footer Installation.

Total Manhours Worked To Date

- 18,328 Hours

Request For Information (RFI's)

- 3 Open RFI's

Submittals

- 4 Open Submittals

Weekly Weather Report

- Working Days Lost This Week: 0
- No Rainy Weather Expected Next Week

Cost Risk Exposure

- CK Continuing To Issue Subcontracts
