


Perry County Courthouse Weekly Summary

Updated 8/23/24



2nd Floor
Courtroom
Plaster
Restoration
8/23/24

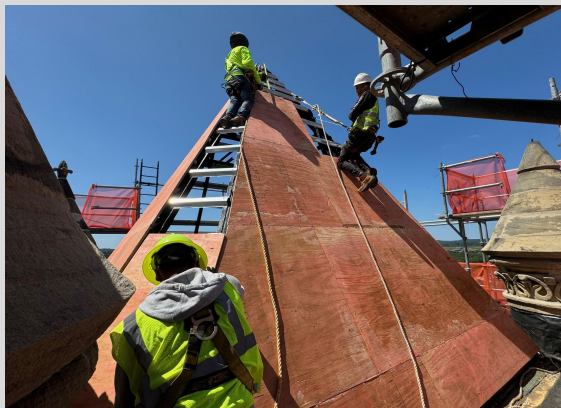

Clock Tower Roof Sheathing 8/22/24



First Floor Door Way Lintel 8/23/24

Construction Activities

- Electricians Continued Roughing In Walls On The Ground, 1st, and 2nd Floor.
- CK Carpenters Continued Wood Restoration On The First Floor And Installed Blocking On The Ground Floor.
- CK Steel Crew Finished Install Of Structural Steel On The Clock Tower Roof.
- Plaster Crew Continued Patching On The Ground Floor And 2nd Floor Courtroom
- Painters Continued Priming New Wood Base.
- Exterior Masons Finished Tuckpointing And Washing The Clock Tower Masonry.
- Interior Masons Installed Remaining Doorway Lintels.
- Roofers Installed Roof Sheathing And Membrane On The Clock Tower.

Total Manhours Worked To Date

- 28,931 Hours

Request For Information (RFI's)

- 6 Open RFI's

Submittals

- 10 Open Submittals
- 3 Late Submittals

Weekly Weather Report

- Working Days Lost This Week: 0

Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
