

Perry County Courthouse Weekly Summary


Updated 9/13/24



Lateral Beam Bracing Install 9/13/24



Clock
Tower Roof
9/13/24

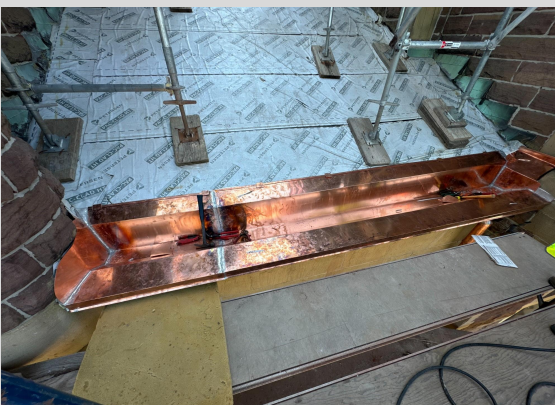

Main Roof Copper Gutter Install 9/13/24

Construction Activities

- Electricians Continued Roughing In Walls On The Ground, 1st, And 2nd Floor.
- CK Carpenters Continued Wood Restoration.
- CK Steel Crew Began Lateral Steel Install On The 2nd Floor.
- Plaster Crew Continued Creating Plaster Molds On The 1st Floor And Continued Installing Plaster Base On The Ground Floor.
- Painters Continued Priming Throughout The Courthouse.
- Exterior Masons Finished Disassembly Of Clock Tower Clock Face's.
- Interior Masons Continued Elevator Shaft Erection.
- Roofers Continued Roof Tile And TPO Roofing Install On The Clock Tower Roof.
- Demo Crew Continued 2nd Floor Ceiling Jack Arch Demo.
- Plumbers Continued Ground Floor Rough In, And Began 1st Floor In Wall Plumbing.

Total Manhours Worked To Date

- 32,089 Hours

Request For Information (RFI's)

- 8 Open RFI's

Submittals

- 2 Open Submittals

Weekly Weather Report

- Working Days Lost This Week: 0

Cost Risk Exposure

- CK Continuing To Issue Subcontracts.
