


# Perry County Courthouse Weekly Summary

Updated 6/6/25



Intermediate Tower Stair Platform 6/6/25

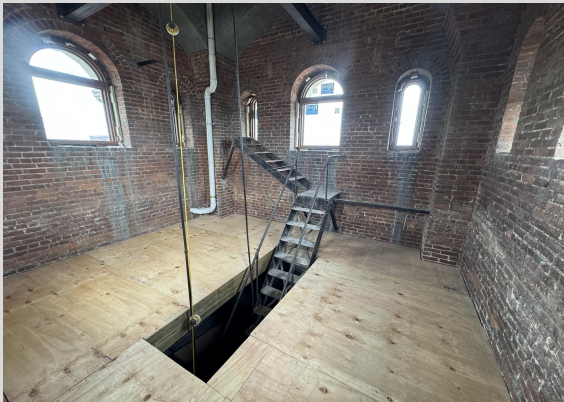

1<sup>st</sup> Floor Courtroom Carpet 6/6/25



Eagle Medallion Install 6/6/25

## Construction Activities

- Electricians Continued Began Installing Lights On The 1<sup>st</sup> And 2<sup>nd</sup> Floors And Continued Exterior Work .
- HVAC Crew Continued Ductwork On The 1<sup>st</sup> Floor And Refrigeration Lines In The Attic.
- CK Framers Continued Framing Install And Drywall On The 2<sup>nd</sup> Floor.
- CK Carpenters Continued Door Casing And Began Installing Door Hardware. Graves Lumber Carpenters Installed The Intermediate Tower Stair Platform.
- Plumbers Continued To Install Bathroom Fixtures.
- CK Concrete Crew Poured The NW Sidewalk.
- Painters Continued Painting The Doors On The Ground Floor And Ceilings On The 1<sup>st</sup> Floor & 2<sup>nd</sup> Floor
- Plasterers Installed The Eagle Medallion In The 1<sup>st</sup> Floor Corridor.
- Flooring Crew Began Laying Carpet In The 1<sup>st</sup> Floor Courtrooms.
- Roofers Continued TPO On The Eastern Roof.

## Total Manhours Worked To Date

- 74,020 Hours

## Request For Information (RFI's)

- 5 Open RFI's

## Submittals

- 9 Open Submittals

## Weekly Weather Report

- Working Days Lost This Week: 0

## Cost Risk Exposure

- CK Working Through Costs Associated With Design Changes.
