


Perry County Courthouse Weekly Summary


Updated 7/18/25



Exterior
Door
Frame
Install
7/18/25

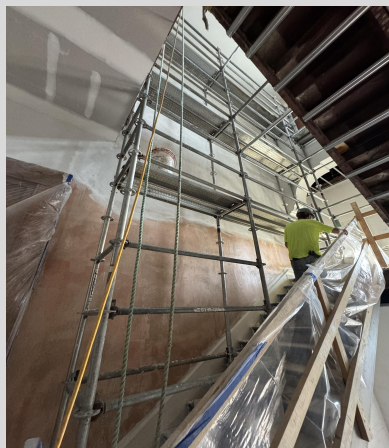

Historic
Stairwell
Plaster
Install
7/18/25

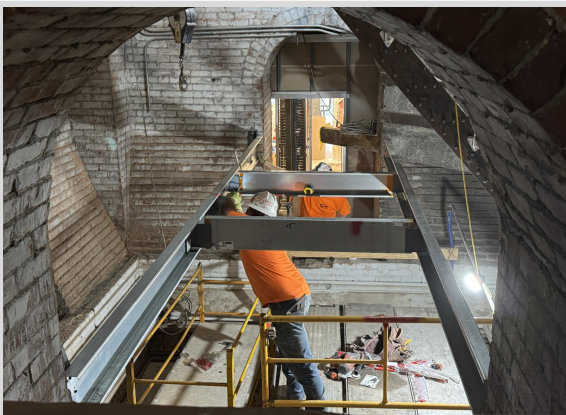

Cove Ceiling Install 7/18/25

Construction Activities

- Electricians Continued Installing Lights & Devices On All Floors.
- HVAC Crew Working on Equipment startup on all floors.
- Ck Framers Continued access panel and cove ceiling installation.
- Ck Carpenters Continued Installment Of Door Hardware, Transaction Couter Woodwork, And Installing Exterior Doors.
- Painters Continued Final Coats On The Ground And 1st Floors.
- Faux Painter Continued Painting Corridor Walls On The 1st Floor.

Total Manhours Worked To Date

- 81,119.38 Hours

Request For Information (RFI's)

- 6 Open RFI's

Submittals

- 8 Open Submittals

Weekly Weather Report

- Working Days Lost This Week: 0

Cost Risk Exposure

- CK Working Through Costs Associated With Design Changes.
