


Perry County Courthouse Weekly Summary

Updated 8/1/25



Historic Stair Handrail Install 8/1/25

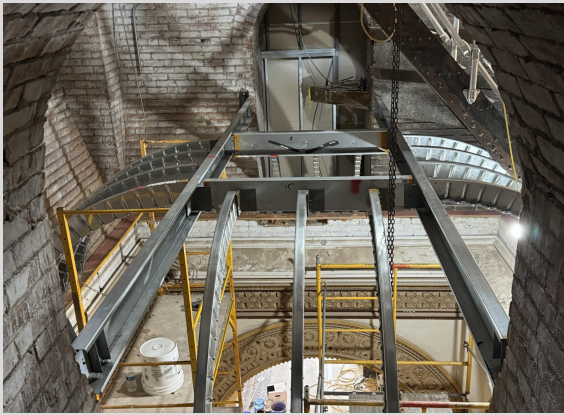

Cove Framing Install 8/1/25



Clock Tower
Ladder
Install
8/1/25

Construction Activities

- Electricians Continued Installing Lights & Devices On All Floors.
- HVAC Crew Working On Equipment Startup On All Floors.
- Ck Framers Continued Access Panel And Cove Ceiling Installation.
- Ck Carpenters Continued Installment Of Door Hardware, Transaction Couter Woodwork, And Historic Stair Newel Posts.
- Ck Iron Workers Finished Handrail Install On The Historic Stair And Began The Clock Tower Ladder Installation.
- Roofers Continued East TPO Roof.
- Elevator Technicians Continued The Elevator Installation.
- Painters Continued Final Coats On The 1st And 2nd Floors.

Total Manhours Worked To Date

- 83,268.38 Hours

Request For Information (RFI's)

- 2 Open RFI's

Submittals

- 3 Open Submittals

Weekly Weather Report

- Working Days Lost This Week: 0

Cost Risk Exposure

- CK Working Through Costs Associated With Design Changes.
